

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	29 September 2026
Project Name	Metro Ticket Generating System in ServiceNow
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Catalog & Form Setup	USN-1	Create Metro Ticket Catalog Item	3	High	Project Team
Sprint-1	Catalog & Form Setup	USN-2	Configure Source, Destination, Passenger Type and Ticket Count variables	3	High	Project Team
Sprint-1	Catalog & Form Setup	USN-3	Configure UI Policies / basic Catalog Client Scripts	3	High	Project Team
Sprint-2	Fare Logic, Flow & Data	USN-4	Implement fare and station mapping logic	5	High	Project Team
Sprint-2	Fare Logic, Flow & Data	USN-5	Build Flow Designer automation	5	High	Project Team
Sprint-2	Fare Logic, Flow & Data	USN-6	Create Metro Database custom table and variable mapping	3	High	Project Team
Sprint-2	Fare Logic, Flow & Data	USN-7	Create / maintain Request and RITM processing	2	Medium	Project Team
Sprint-3	QR, Portal & Access	USN-8	Implement QR-based digital ticket	5	High	Project Team
Sprint-3	QR, Portal & Access	USN-9	Implement Service Portal widget / spModal ticket display	3	High	Project Team
Sprint-3	QR, Portal & Access	USN-10	Configure request tracking and ticket visibility	2	Medium	Project Team
Sprint-3	QR, Portal & Access	USN-11	Configure roles and ACL access	3	High	Project Team
Sprint-4	Testing, Debugging & Deployment	USN-12	Test fare calculations and variable-to-field mappings	3	High	Project Team
Sprint-4	Testing, Debugging & Deployment	USN-13	Use Flow Execution Details to debug workflow failures	2	Medium	Project Team
Sprint-4	Testing, Debugging & Deployment	USN-14	Perform QR / portal compatibility testing	3	High	Project Team
Sprint-4	Testing, Debugging & Deployment	USN-15	Perform UAT and role/security testing	3	High	Project Team

Sprint-4	Testing, Debugging & Deployment	USN-16	Prepare deployment / recreation documentation for a new PDI	5	High	Project Team
----------	---------------------------------	--------	---	---	------	--------------


Project Tracker, Velocity & Burndown Chart

Sprint	Total Story Points	Duration	Sprint Start	Sprint End (Planned)	Story Points Completed	Release Status
Sprint-1	9	5 Days	Day 1	Day 5	9	Completed
Sprint-2	15	5 Days	Day 6	Day 10	15	Completed
Sprint-3	13	5 Days	Day 11	Day 15	13	Completed
Sprint-4	16	5 Days	Day 16	Day 20	16	Completed

Velocity

Total completed story points = 53. Number of sprints = 4. Average team velocity = $53 / 4 = 13.25$ story points per sprint.

Burndown Chart

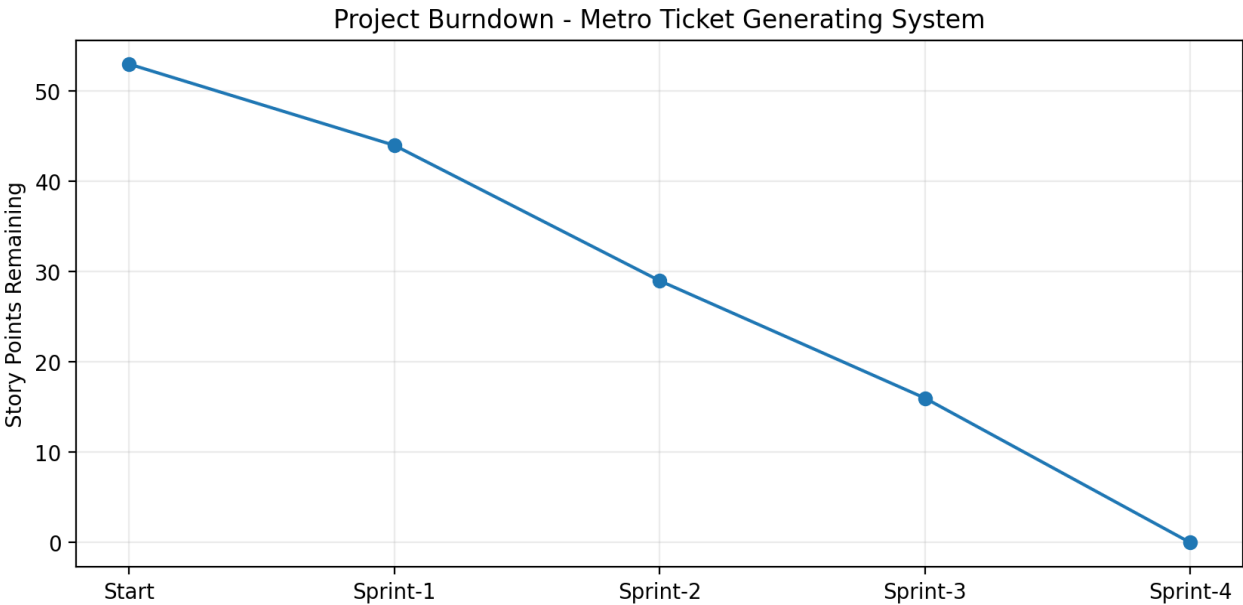

The burndown chart shows the remaining story points after each completed sprint. Because the project material did not provide exact historical calendar dates, the tracker uses a relative 20-day schedule (four 5-day sprints) while preserving the sprint sequence and completed work structure.

Sprint Release Summary

Sprint	Release Outcome
Sprint-1	Catalog item and booking-form foundation completed.
Sprint-2	Fare logic, Flow Designer, RITM/request processing, and Metro Database mapping completed.
Sprint-3	QR ticket, Service Portal display, request visibility, roles and ACL configuration completed.
Sprint-4	Fare/variable debugging, flow diagnostics, QR testing, UAT, security testing, and deployment documentation completed.
